


Appendix B – Detailed Timeline

Approach & Timing	Summer 2025	September 2025	Fall 2025	End of 2025	Early 2026	Mid 2026	Fall 2026	End of 2026
Previous Timeline	<ul style="list-style-type: none">Phase 3 Consultation on 3 concepts;3 readings for Loan Authorization Bylaw	<ul style="list-style-type: none">Results of WWHR Phase 3;Council decision on: (a) preferred concept (b) elector approval method;Continue design development	Required elector approval process for municipal borrowing (AAP or referendum)	<ul style="list-style-type: none">Certification of results of elector approvalAdoption of Loan Authorization Bylaw	Possible rezoning process	Construction Tender issued	Project Kick Off (August)	Project underway
Current Timeline		<ul style="list-style-type: none">Results of WWHR Phase 3;Council decision on conceptContinue design developmentLoan Authorization Bylaw Adoption		Possible rezoning process		Construction Tender issued	Project Kick Off (August)	
Voluntary Plebiscite		<ul style="list-style-type: none">Results of WWHR Phase 3;Council decision on voluntary elector inputLoan Authorization Bylaw Adoption	Voluntary plebiscite process (up to 2 advance opportunities, mail ballots and one general voting day)	<ul style="list-style-type: none">Receive results of plebisciteSelection of preferred concept			Construction Tender issued	Project Kick Off* (Nov-Dec)

*\$550,000 cost escalation, plus \$80,000 for plebiscite

Previous timeline

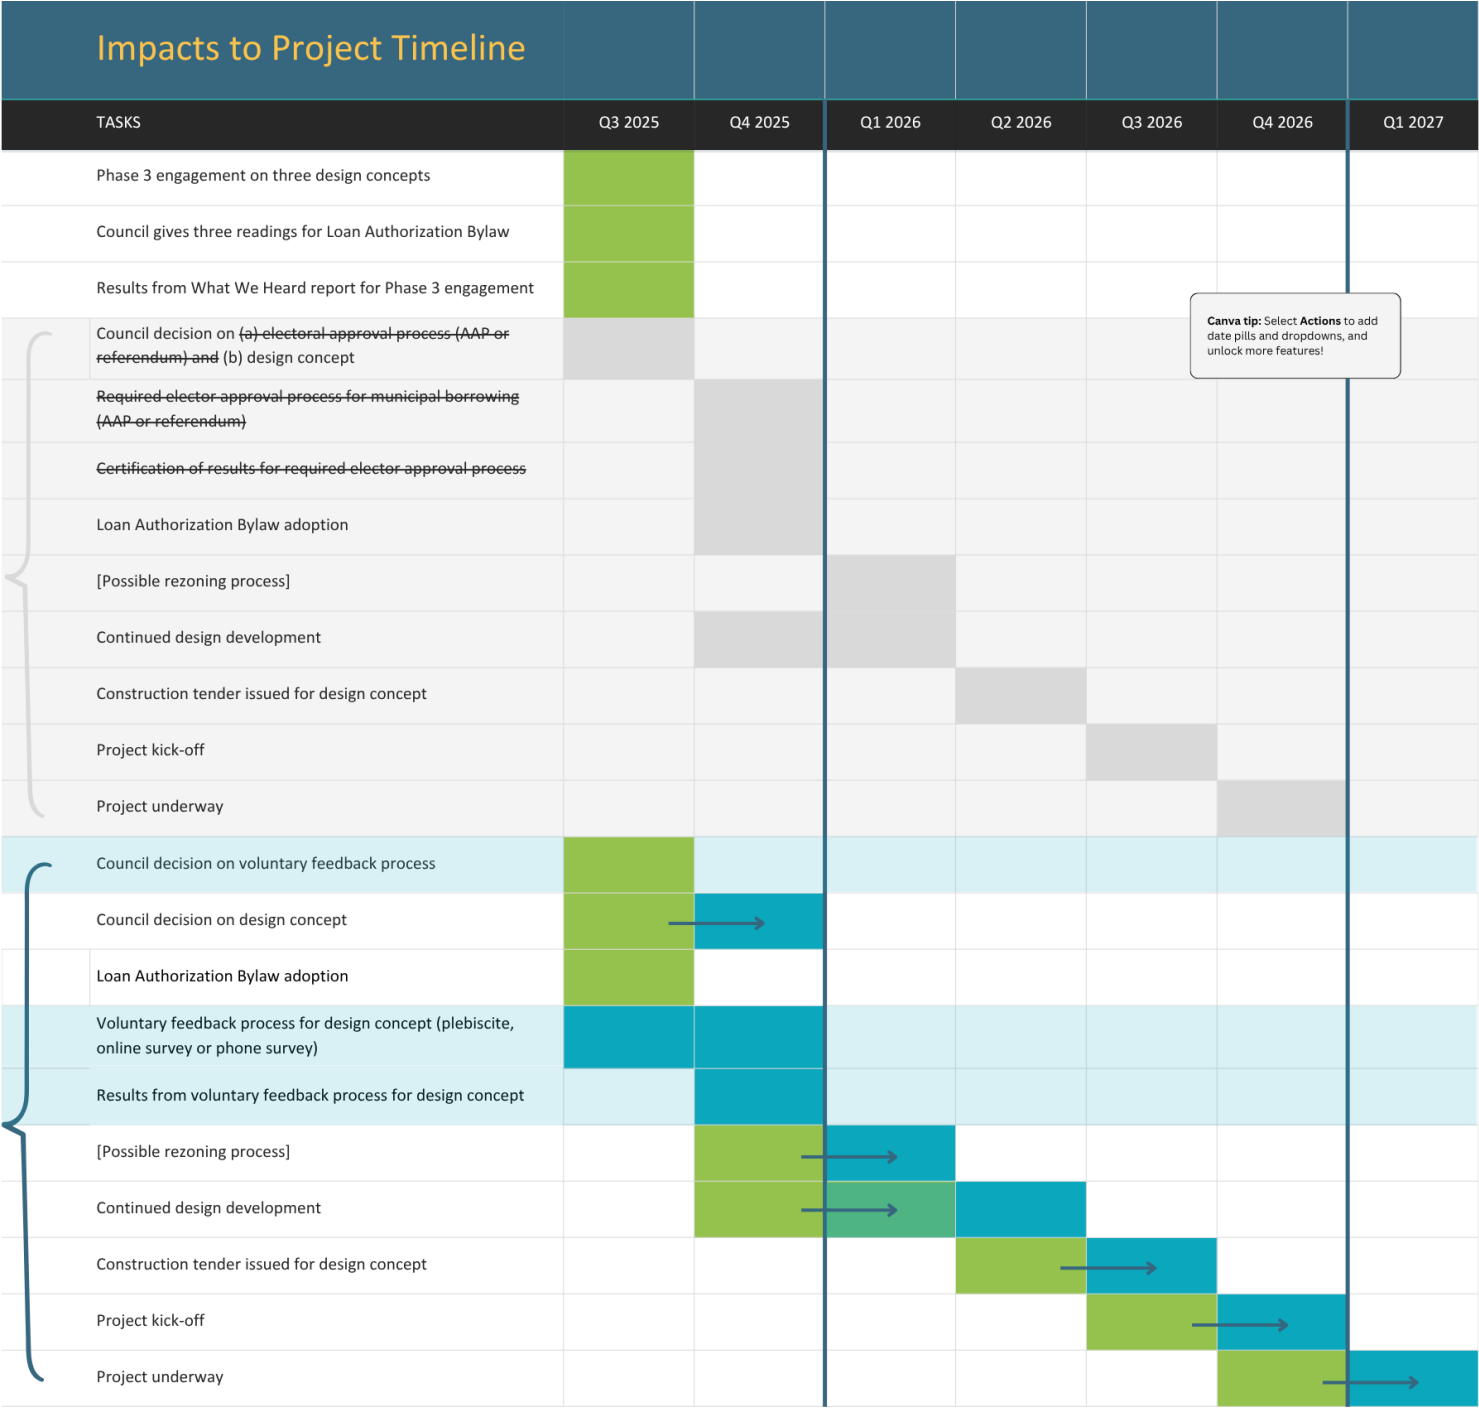

Canva tip: Select Actions to add date pills and dropdowns, and unlock more features!

Updated timeline
(blue = timeline delay with voluntary plebiscite process)

Project kick-off delay from Aug 2026 to Nov/Dec 2026
